

BONDI PAVILION RESTORATION AND CONSERVATION PROJECT




Bondi Pavilion – Upcoming Works

Upcoming Works

- Install protection to heritage items including floor mosaics
- Structural demolition
- Removal of outdoor benches and ceramic tile murals on the northern wall of the Atrium—
to be provided to Council for salvage
- Structural demolition of steel structure in The Bucket List
- Commence underpinning works
- Services disconnection
- Removal of redundant services

Progress Photos

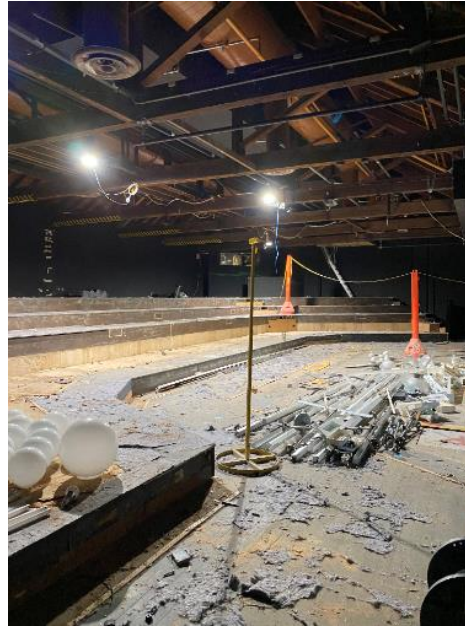

Bondi Pavilion – Short Range Milestones

- Protection of heritage stairs and Seagull room floors complete by 7th August
- Western concrete external staircases to Main Pavilion removed by 12th August
- Bucket List awning steel structure removed by 14th August
- Slab removal in South Pavilion Building by 14th August
- Service trades mobilized on site by 14th August
- Removal of existing signage by 26th August

Bondi Pavilion – Completed Works

- Soft strip out and rubbish removal to all buildings
- Hoarding Installation
- Service disconnection

Bondi Pavilion

